


REBUILDING I-93 SALEM TO MANCHESTER



10418H: EXIT 3 PARK & RIDE

PROJECT OVERVIEW: Contract 10418H will construct a new Park and Ride facility in the area of Exit 3, just east of the I-93 northbound off-ramp in Windham, creating over 130 spaces for vehicles. Access to the Park and Ride will be from the newly constructed portion of NH 111A. This new Park and Ride will replace the temporary Park and Ride that was at the intersection of NH 111 and Wall Street.

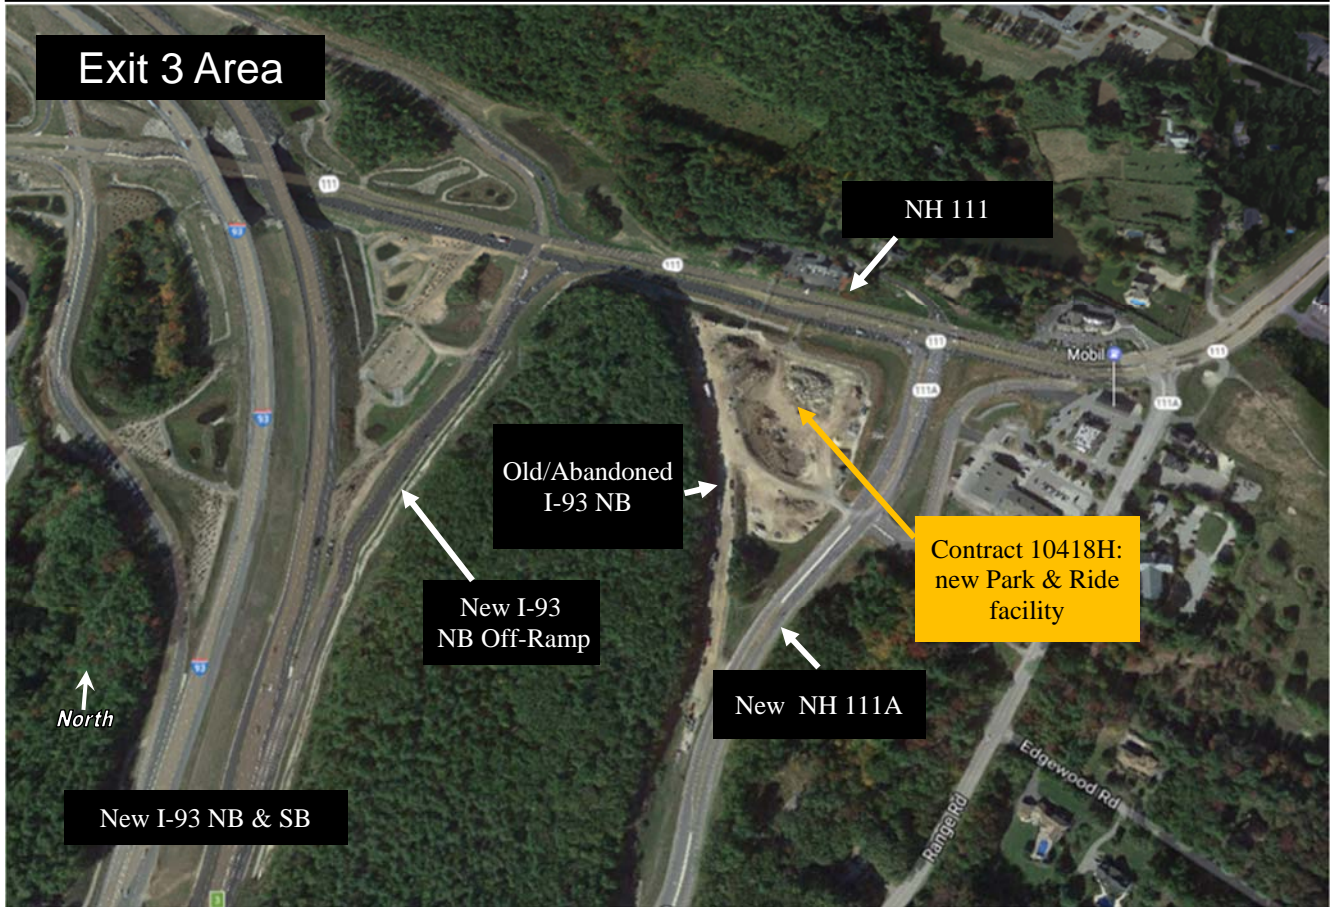

PROJECT FACT SHEET

Updated: 4-27-17

PROJECT SCHEDULE

% Complete: 33%


Recent Activities: Drainage work and excavation for the parking area sub-grade is nearing completion. Blasting is complete. Some of the resulting material from blasting is being transported north along I-93 to project 14633B (between the weigh station and Kendall Pond Road) to be used for widening of the highway there.

Upcoming Activities: Drainage work and excavation for the subgrade will continue.

PROJECT FACTS	CONTRACT: 10418H
Advertised Date:	August 30, 2016
Award Date:	Nov. 16, 2016
Construction Start Date:	Nov. 28, 2016
Est. Completion Date:	Oct. 27, 2017
Bid Price:	\$1.6M
Total Est. Construction Cost: bid plus inspection, testing, oversight	\$2.1M
Contractor: George R. Cairns and Sons, Inc.	



RebuildingI93.com

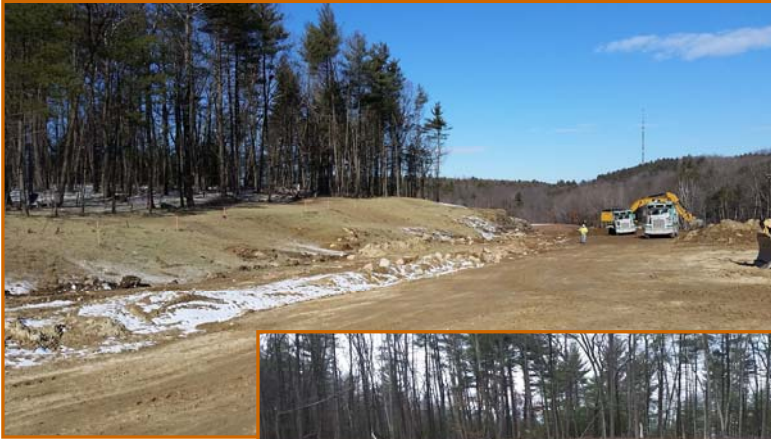

LEFT: EXCAVATION OF BLASTED ROCK

BELOW, MIDDLE: LOOKING AT LAST AREA TO BE BLASTED



RIGHT: LOADING ROCK

BELOW: SITE WORK AT THE NEW PARK AND RIDE AREA

