

REBUILDING I-93 SALEM TO MANCHESTER



EXIT 5 ~ SOUTHBOUND RAMPS, NORTHBOUND ON-RAMP & BRIDGES LONDONDERRY

CONSTRUCTION
COMPLETE



Looking North Along the New NB On-Ramp 04-28-2010

PROJECT OVERVIEW:

This project involves the reconstruction/reconfiguration of Exit 5 southbound on and off-ramps and the northbound on-ramp. The existing northbound off-ramp will be replaced under a subsequent contract. The three new ramps will help improve the interchange capacity and improve safety on the mainline, and are necessary for the future replacement of four "red list" bridges located within the interchange. Work started on this project in July 2008, and completed May 2010.



PROJECT FACT SHEET



STORMWATER TREATMENT SOLUTIONS

PROJECT FACTS

CONTRACT: 14633E

Advertised Date:	April 22, 2008
Award Date:	June 25, 2008
Start Construction	July 2008
Completion Date (Est.)	Spring 2010
Bid Price:	\$14.9M
Total Construction Cost:	\$16.1M
Contractor:	Severino Construction

PROJECT SCHEDULE

CONTRACT: 14633E

% Complete: 100%

Recent Activities: Detention basin #15 was completed, landscaping and final cleanup were done.


Updated 05-21-2010



Visit RebuildingI93.com to sign up for automatic email notifications of important traffic information.

RebuildingI93.com

MOVING
AHEAD

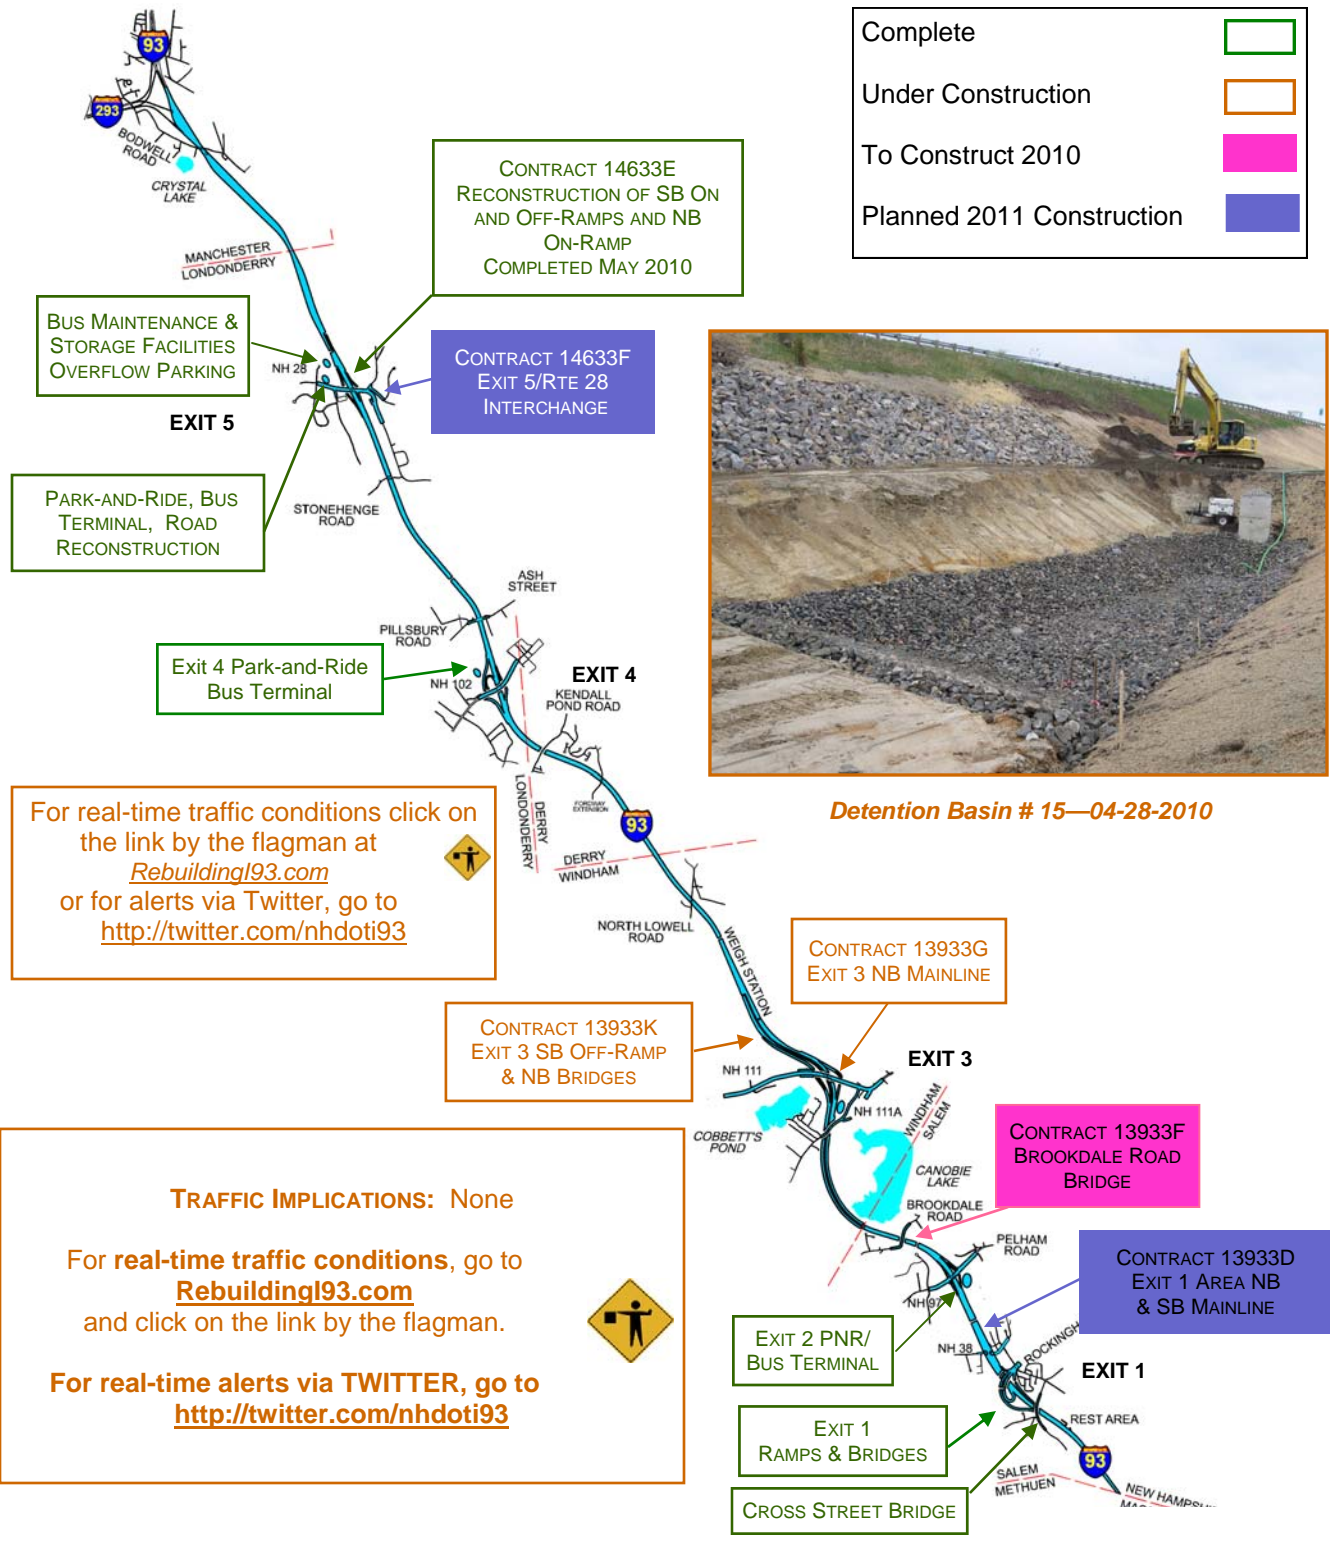

For real-time traffic conditions click on the link by the flagman at RebuildingI93.com or for alerts via Twitter, go to <http://twitter.com/nhdoti93>

TRAFFIC IMPLICATIONS: None

For real-time traffic conditions, go to RebuildingI93.com and click on the link by the flagman.

For real-time alerts via TWITTER, go to <http://twitter.com/nhdoti93>

