


# REBUILDING I-93 SALEM TO MANCHESTER



## 14633B: NB & SB MAINLINE WIDENING WEIGH STATION TO KENDALL POND ROAD

PROJECT FACT SHEET

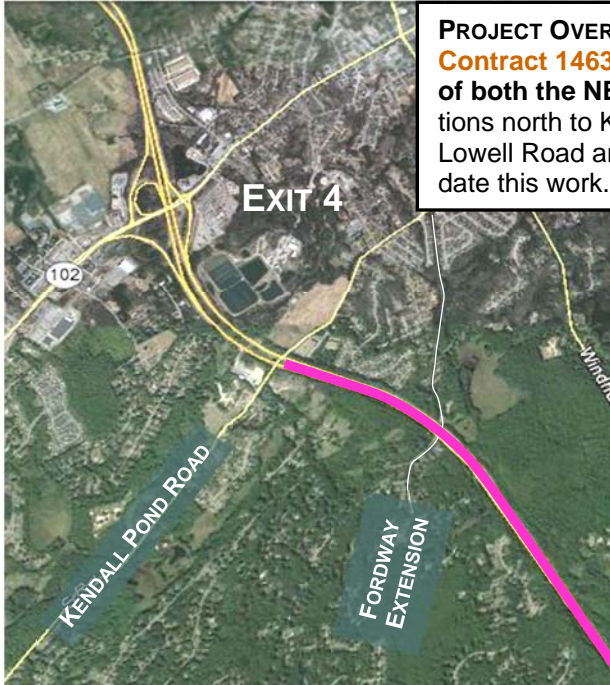

### PROJECT OVERVIEW:

**Contract 14633B** will reconstruct and widen approximately **3.5 miles** of both the **NB and SB** lanes of I-93 from approximately the weigh stations north to Kendall Pond Road. Four bridges, I-93 NB & SB over North Lowell Road and over Fordway Extension, will be widened to accommodate this work.

PROJECT FACTS	CONTRACT: 14633B
Advertised Date:	<b>November 10, 2015</b>
Award Date:	<b>February 10, 2016</b>
Start Construction Date:	<b>February 17, 2016</b>
Est. Completion Date:	<b>October 25, 2019</b>
Bid Price:	<b>\$49.4M</b>
Total Est. Construction Cost: (bid plus inspection, testing, oversight, etc.)	<b>\$54.4M</b>
Construction is funded with a \$200M TIFIA Loan.	
Contractor: R.S. Audley, Inc.	

### PROJECT SCHEDULE

% Complete: 43%

**Recent Activities:** The project progressed with major construction activities such as blasting work, embankment work, tree clearing and drainage detention basins. Bridge work began on the east side of the NB Fordway Ext. Bridge, bridge demolition began at the NB North Lowell Road Bridge and bridge beams were set. The extension of the Recreation Trail box culvert to the median is completed. A NB soundwall berm has also been completed.

**Upcoming Activities:** Blasting will continue throughout the project to produce materials needed for roadway construction. Bridge work will continue at NB North Lowell Road Bridge with deck panels placement. Soundwall construction will continue, including the wall panel installation. The construction of a NB crossover to the SB barrel continues to allow for a future traffic shift to the west.

Updated: 4-27-17



[RebuildingI93.com](http://RebuildingI93.com)

MOVING  
AHEAD





*NB NORTH LOWELL RD BRIDGE WORK.*



*REC TRAIL BOX CULVERT CONSTRUCTION IN MEDIAN*



*I-93, NEW AND OLD, FACING SOUTH.*



*NB SOUNDWALL BASES, FACING NORTH.*



*NEW NB ALIGNMENT, FACING NORTH.*

14633B



[RebuildingI93.com](http://RebuildingI93.com)

MOVING  
AHEAD
